

Work Order ID 83477

April-18-12 2:41:18 PM

83477

Page 1

Item ID: D3166-1

Accept

N900040100

Setup Start

NS1

Revision ID:

Item Name: Basket Hoop

Stop

NS2

Start Date: 18/04/2012 Start Qty: 10.00

10

Cust Item ID:

Required Date: 02/05/2012 Req'd Qty: 10.00

10

Customer:

Reference:

Approvals: Process Plan: MLJ

Date: 12/04/10

Tooling:

Date:

Run Start

NR1

QC:

Date:

SPC (Y/N):

Date:

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3166	Rev A1

100		0.00							
100	Skidtubes								
Large Fab	Memo	0.00							
Large Fab	Cut 3/4" x 3/4" square tubing 60.00" long.								

25

13-03-08

DAS
09
9-89

110		0.00							
110	BENDING MACHINE - SKIDTUBES								
CNC Bend 1	Memo	0.00							
CNC Delta 100 Bender	Form D3166-1 Basket Hoop as per Dwg D3166 using Bending program 350 BASB, and folio 18.								

20

13-03-10 SAD

120		0.00							
120	QC6- Inspect dimensions to drawing								
QC	Memo	0.00							
Quality Control	Inspect Basket Hoop dimensions with template D3166-1-T1 (DT8302)								

20x

DAS
24
9-89

CP13-3-15

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Work Order ID 83477

83477

Page 2

April-18-12 2:41:18 PM

Item ID: D3166-1

Accept

N900040100

Setup Start ***NS1***

Revision ID:

Item Name: Basket Hoop

Stop ***NS2***

Start Date: 18/04/2012 Start Qty: 10.00

10

Cust Item ID:

Required Date: 02/05/2012 Req'd Qty: 10.00

10

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start ***NR1***
Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
130	Identify as per dwg & Stock Location: <u>WA 4</u>	0.00							
130									
Packaging	Memo	0.00							
Packaging									
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.00							
Quality Control									

GL13.315

20x

13/3/20

13-03-19

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

Picklist Print

April-18-12 2:41:22 PM

Page 1

Work Order ID: 83477

83477

Parent Item: D3166-1

D3166-1

Parent Item Name: Basket Hoop

Start Date: 18/04/2012

Required Date: 02/05/2012

Start Qty: 10.00

Required Qty: 10.00

Comments:

IPP A02.08.23New issueKJ

IPP: B 08.12.05 Updated bending program on step 3 per NCR W/O43165 KJ

Verified by: EC

IPP Rev:C 09-01-23 as per DEO D3166-A2 DD verified by:EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M304TS0.750W.065		Purchased	No			100	f	1,013.792	5	52.63158			

M304TS0 750W 065

304 SQ Tube .75x.75x.065W

**

13-03-08 AD

Location	Loc Qty	Loc Code
MAT017	553.7325342	
120267	53.7325342	
120633	500	
MAT018	453.40289	
121170	412.40289	
7636	41	
WA007	0.5907428	
116763	0.5907428	
WA035	6.0667	
118181	6.0667	

M124069 -> 105.2631

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries



DESIGN #	DRAWN BY CP	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
CHECKED #	APPROVED #	DRAWING NO. D3166	REV. A SHEET 1 OF 1
DATE 02.07.10		TITLE BASKET HOOP	SCALE NTS
A	02.07.10	NEW ISSUE	
A1	04.04.08	38+/-1 WAS 36.0	

RELEASED
02.08.06


DEO ATTACHED



10.6 (REF, NEED 8.0 MIN)

D3166-1 BASKET HOOP

- 1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 60.00" LONG
(REF DART SPEC. M304TS0.750W.063)
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS
OTHERWISE NOTED

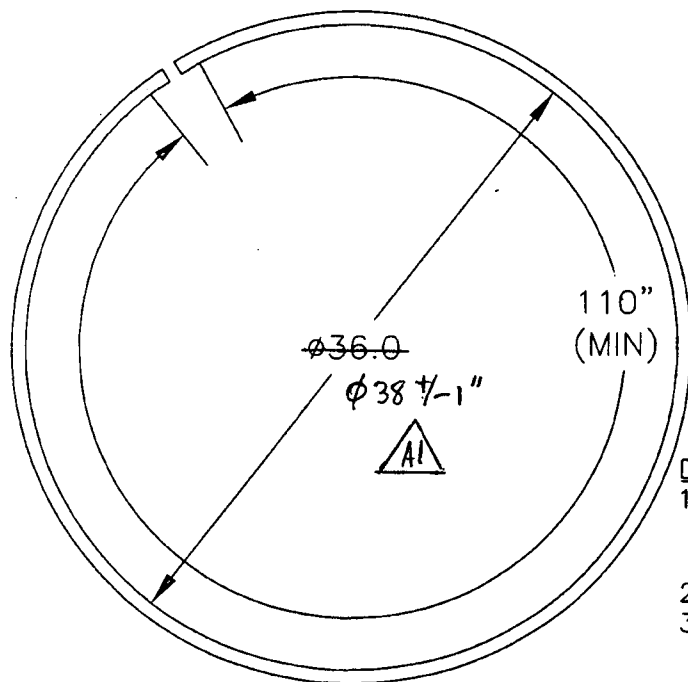

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 83977 M.C.
12/04/18

D3166-3 BASKET HOOP

- 1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 120.00" LONG
(REF DART SPEC. M304TS0.750W.063)
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS
OTHERWISE NOTED

Copyright © 2002 by DART AEROSPACE LTD

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries

DRAWING NO. D3166	TITLE BASKET HOOP	REV A1	DART AEROSPACE LTD ENGINEERING ORDER		D.E.O. NO. D3166-A-2	SHEET NO. 1 OF 1	SCALE NTS
DRAWN AJS	CHECKED 1	MFG. APPR. M	APPROVED MP		DE APPR. H		
DATE 08.12.11	DATE 08.12.15	DATE 08/12/15	DATE 08/12/16		DATE 08.12.16		

1) MODIFY MATERIAL NOTE FOR D3166-1 AS SHOWN:

IS:

1) MATERIAL: AISI 304/316 SS, 3/4 X 3/4 X 0.065 WALL SQUARE TUBING,
60.00" LONG
REF. DART SPEC M304TS0.750W.065

83477

WAS:

1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 60.00" LONG
(REF DART SPEC. M304TS0.750W.063)

2) MODIFY MATERIAL NOTE FOR D3166-3 AS SHOWN:

IS:

1) MATERIAL: AISI 304/316 SS, 3/4 X 3/4 X 0.065 WALL SQUARE TUBING,
120.00" LONG
REF. DART SPEC M304TS0.750W.065

WAS:

1) MATERIAL: AISI 304/316 SS SQUARE TUBING,
0.75" x 0.75" x 0.063 WALL, 120.00" LONG
(REF DART SPEC. M304TS0.750W.063)

RELEASED
08/12/16 MP

0

REASON: SEE PAR 08-005

W/O:		WORK ORDER CHANGES					
DATE	STEP	PROCEDURE CHANGE	By	Date	Qty	Approval Chief Eng / Prod Mgr	Approval QC Inspector

Part No: _____ PAR #: _____ Fault Category: _____ NCR: Yes No DQA: _____ Date: _____

Resolution: _____ Disposition: _____ QA: N/C Closed: _____ Date: _____

NCR:		WORK ORDER NON-CONFORMANCE (NCR)						
DATE	STEP	Description of NC Section A	Corrective Action Section B			Verification Section C	Approval Chief Eng	Approval QC Inspector
			Initial Chief Eng	Action Description Chief Eng	Sign & Date			

NOTE: Date & initial all entries
